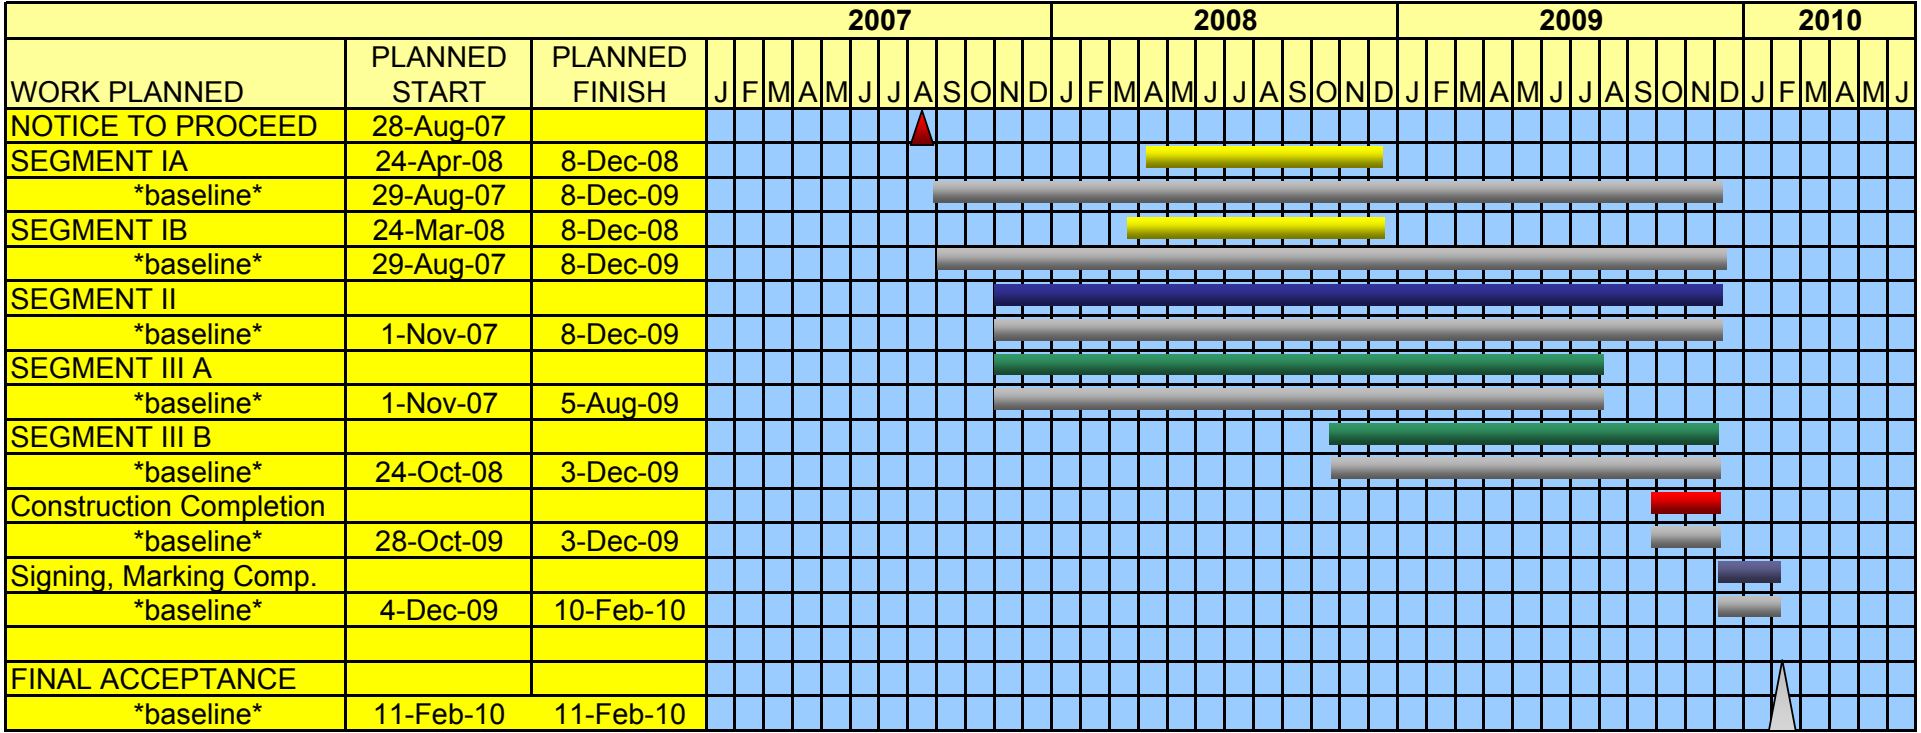
2007
2008
2009
2010
J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J
WORK PLANNED
PLANNED START
PLANNED FINISH
NOTICE TO PROCEED 28-Aug-07
SEGMENT IA 24-Apr-08 8-Dec-08
baseline 29-Aug-07 8-Dec-09
SEGMENT IB 24-Mar-08 8-Dec-08
baseline 29-Aug-07 8-Dec-09
SEGMENT II
baseline 1-Nov-07 8-Dec-09
SEGMENT III A
baseline 1-Nov-07 5-Aug-09
SEGMENT III B
baseline 24-Oct-08 3-Dec-09
Construction Completion
baseline 28-Oct-09 3-Dec-09
Signing, Marking Comp.
baseline 4-Dec-09 10-Feb-10
FINAL ACCEPTANCE
baseline 11-Feb-10 11-Feb-10
